

# MONTHLY CONSTRUCTION MANAGER'S REPORT



# Foster City Levee Improvements Project City Project No. CIP 301-657



Contractor:	Shimmick Construction Co	Report Period: March 1-31, 2023
CM:	Tanner Pacific, Inc.	
Designer:	Schaaf & Wheeler	

Contract/Schedule Update							
Original Contract  Duration (Calendar Days):	1200	Additional Days Granted:	0	Calendar Days Remaining:	316		
Days Elapsed:	884	% Elapsed:	73.7%				
Notice To Proceed:	9/28/2020	Substantial Completion Date:	10/2/2023	Final Completion Date:	1/10/2024		
Cost Management Update							
Original Contract Value:	\$60,218,000.00	Approved CCOs:	\$ 11,974,271.21	Revised Contract Value:	\$72,192,271.21		
Contingency:	\$12,491,635.92	Remaining Contingency:	\$517,364.71	% Contingency Used*:	96%		
Costs Billed to Date:	\$ 57,331,707.69	% of Contract Billed to Date:	79%				



### MONTHLY CONSTRUCTION MANAGER'S REPORT



#### **Work Summary**

#### **Recently Completed:**

- Initial earthwork for subgrade from Sta. 56+00 64+00
- Continued construction of Retaining Wall 02 (northwest of the SM Bridge)
- Retaining Wall 4 construction at Access Point 10 north of the SM Bridge
- Bayside access path concrete placement from Access Point 12- Sta. 118+25 along Beach Park Blvd
- Irrigation controls near Shorebird Park
- Pulling of wire for electroliers along Beach Park Blvd
- Trail opening from ~Sta. 205+00 343+00 (Foster City Blvd to Southern Project Limit)
- Irrigation work from ~Sta. 205+00 343+00 (Foster City Blvd to Southern Project Limit)
- Final trail signage installation from ~Sta. 200+00 -Sta. 343+00 (south of Shorebird Park)
- Trail striping from ~Sta. 205+00 343+00 (Foster City Blvd to Southern Project Limit)
- Irrigation connections along Beach Park Blvd (2) and E. 3<sup>rd</sup> Ave (1)

#### **Upcoming:**

- Continued submittals for signage, site furnishings, and shade structures
- Continued import of materials to staging areas
- Access Point 02 ramp completion (near Baywinds Park)
- Continued construction of sheet pile wall concrete caps north of the SM Bridge)
- Continued construction of bay-side paths north of the SM Bridge
- Installation of shade structures near Access Point 17 along Beach Park Blvd
- Continued guardrail and handrail installation along Beach Park Blvd
- Completion of fine grading along Beach Park Blvd
- Pavement installation from San Mateo Bridge to Foster City Blvd
- Striping and signage installation along Beach Park Blvd
- Handrail and guardrail installation along Beach Park Blvd
- Trench drain installations along Beach Park Blvd
- Removal of K-rail along Beach Park Blvd
- Slurry seal and restriping of Beach Park Blvd
- Continued access point flatwork (concrete ramps and stairs) along Beach Park Blvd
- Wiring and energizing of streetlights along Beach Park Blvd
- Installation of landscape soil preparation work for ornamental plantings around Access Points along Beach Park Blvd
- Final handrail punch list from ~Sta. 205+00 343+00 (Foster City Blvd to Southern Project Limit)
- Access Point 30 guardrail installation and opening near Wheelhouse Lane
- Final trail signage installation from ~Sta. 205+00 343+00 (Foster City Blvd to Southern Project Limit)




## MONTHLY CONSTRUCTION MANAGER'S REPORT



## **Monthly Progress Photos**



Earthen fill near AP 6 near East 3<sup>rd</sup> Ave

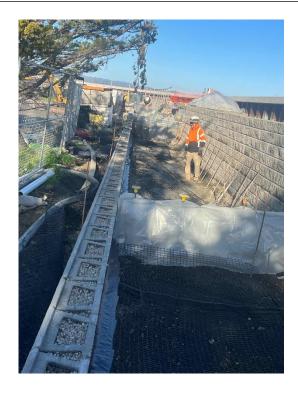

AP 10 retaining wall construction near the San Mateo Bridge



Rebar and formwork for the shade structure foundations along Beach Park Blvd near AP 17



Removal of trail closure fencing near AP 38 Baffin Court
