



MONTHLY CONSTRUCTION MANAGER'S REPORT



Foster City Levee Improvements Project City Project No. CIP 301-657



Contractor:	Shimmick Construction Co	Report Period: September 1-30, 2023
CM:	Tanner Pacific, Inc.	
Designer:	Schaaf & Wheeler	

Contract/Schedule Update					
Original Contract Duration (Calendar Days):	1200	Additional Days Granted:	0	Calendar Days Remaining:	102
Days Elapsed:	1098	% Elapsed:	91.5%		
Notice To Proceed:	9/28/2020	Substantial Completion Date:	10/2/2023	Final Completion Date:	1/10/2024
Cost Management Update					
Original Contract Value:	\$60,218,000.00	Approved CCOs:	\$11,829,679.87	Revised Contract Value:	\$72,047,679.87
Contingency:	\$12,491,635.92	Remaining Contingency:	\$661,956.05	% Contingency Used*:	95%
Costs Billed to Date:	\$ 65,656,340.57	% of Contract Billed to Date:	91%		



MONTHLY CONSTRUCTION MANAGER'S REPORT




Work Summary

Recently Completed:

- *Bayside Access Path completion from AP 4 – AP 5*
- *Artificial turf placement adjacent to FW 4 (near Baywinds Park)*
- *Trail striping and pavement markings north of the SM Bridge*
- *Landscaping and plantings north of the SM Bridge*
- *Handrail and guardrail installation north of the SM Bridge*
- *Chain link fencing installation north of the SM Bridge*
- *Clearing, grubbing, and concrete work at Gateshead Park*
- *Signage installation north of the SM Bridge*
- *Pedestrian Bridge Restoration at Bayside Towers*

Upcoming:

- *Restoration of project staging areas (Sea Cloud Park, Bridgeview Park, & E. 3rd Ave)*
- *Rock slope protection placement north of the SM Bridge near AP 4 – AP 5*
- *Site furnishings north of the SM Bridge*
- *Final punch list work from ~Sta. 205+00 - 343+00 (Foster City Blvd to Southern Project Limit)*
- *Final punch list work from ~Sta. 100+00 - 205+00 (Bridgeview Park to Foster City Blvd)*
- *Final punch list work from ~Sta. 00 - 100+00 (San Mateo City Limit to San Mateo Bridge)*
- *Access Point 31 (lagoon intake structure) completion and opening*
- *O'Neil Slough Sheet Pile Removal*




MONTHLY CONSTRUCTION MANAGER'S REPORT



Monthly Progress Photos



Bayside Path Concrete Placement North of the SM Bridge

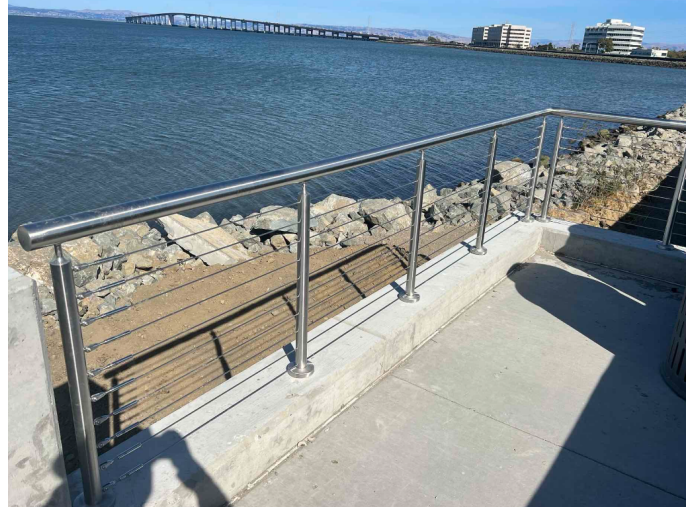

Access Point No. 4 Guardrail Installation



Gateshead Park Restoration



Access Point No. 6 Landscaping
